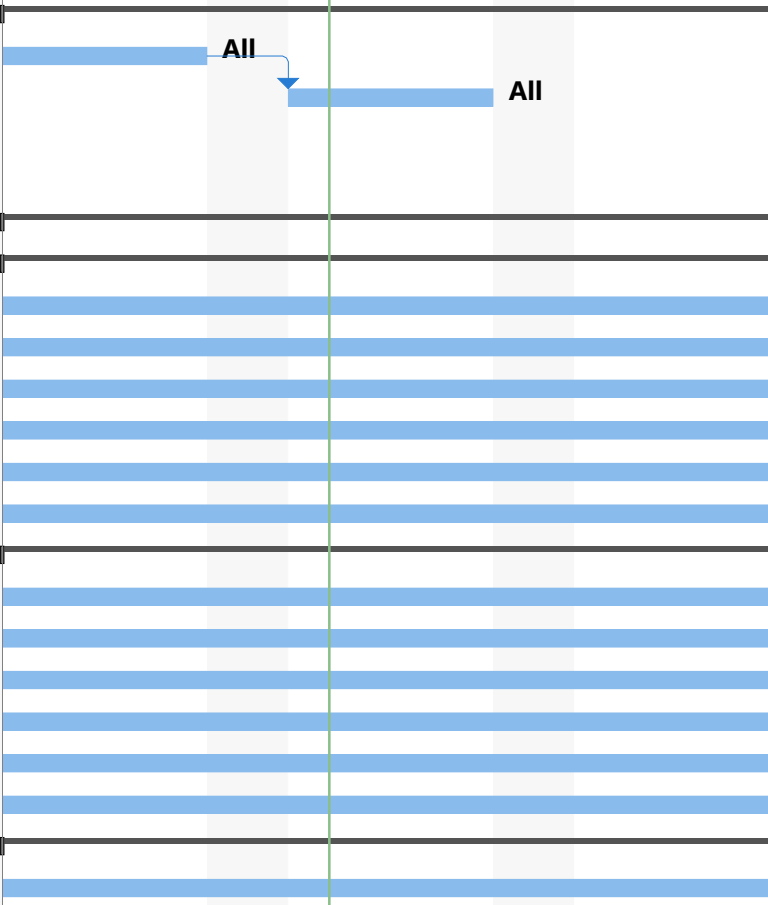



ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	29 Feb '16 7 Mar '16 14 Mar '16 S M T W T F S S M T W T F S S M T W T F													
1			Planning	25 days	Mon 29/02/1	Fri 1/04/16															
2			Task allocation	5 days	Mon 29/02/1	Fri 4/03/16															
3			Gantt chart	5 days	Mon 7/03/16	Fri 11/03/16	2														
4			Budget	5 days	Mon 28/03/1	Fri 1/04/16	6														
5			List of materials	5 days	Mon 28/03/1	Fri 1/04/16	6														
6			Research	20 days	Mon 29/02/1	Fri 25/03/16															
7			Construction	20 days	Mon 29/02/1	Fri 25/03/16															
8			Materials	20 days	Mon 29/02/1	Fri 25/03/16															
9			Type of structure	20 days	Mon 29/02/1	Fri 25/03/16															
10			Technologies	20 days	Mon 29/02/1	Fri 25/03/16															
11			Automatic door	20 days	Mon 29/02/1	Fri 25/03/16															
12			Fixations	20 days	Mon 29/02/1	Fri 25/03/16															
13			Production process	20 days	Mon 29/02/1	Fri 25/03/16															
14			Marketing	20 days	Mon 29/02/1	Fri 25/03/16															
15			SWOT analysis	20 days	Mon 29/02/1	Fri 25/03/16															
16			Segmentation analysis	20 days	Mon 29/02/1	Fri 25/03/16															
17			Marketing strategy	20 days	Mon 29/02/1	Fri 25/03/16															
18			Competitors	20 days	Mon 29/02/1	Fri 25/03/16															
19			Target	20 days	Mon 29/02/1	Fri 25/03/16															
20			Logo/name	20 days	Mon 29/02/1	Fri 25/03/16															
21			Sustainability	20 days	Mon 29/02/1	Fri 25/03/16															
22		 	Type of resource	20 days	Mon 29/02/1	Fri 25/03/16															

Project: ProjectPlanning
Date: Tue 8/03/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	29 Feb '16														7 Mar '16							14 Mar '16						
								S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F								
23				Life cycle	20 days	Mon 29/02/16	Fri 25/03/16																												
24				Eco-efficiency me	20 days	Mon 29/02/16	Fri 25/03/16																												
25				Ethical and deontolog	20 days	Fri 1/04/16	Thu 28/04/16																												
26				Dome design	40 days	Mon 28/03/16	Fri 20/05/16	6																											
27				Brainstorming	5 days	Mon 28/03/16	Fri 1/04/16																												
28				Draw sketch	5 days	Mon 4/04/16	Fri 8/04/16	27																											
29				3D simulation	10 days	Mon 11/04/16	Fri 22/04/16	28																											
30				Cardboard model	10 days	Mon 9/05/16	Fri 20/05/16	29;31																											
31				Calculations	10 days	Mon 25/04/16	Fri 6/05/16	29																											
32				Development and construction	18 days	Mon 23/05/16	Wed 15/06/16																												
33				Blueprinting	2 days	Mon 23/05/16	Tue 24/05/16	26																											
34				Prototyping	5 days	Wed 25/05/16	Tue 31/05/16	26;33																											
35				Testing	2 days	Wed 1/06/16	Thu 2/06/16	34																											
36				Building	5 days	Fri 3/06/16	Thu 9/06/16	35																											
37				Final testing	2 days	Fri 10/06/16	Mon 13/06/16	36																											
38				Final adjustments	2 days	Tue 14/06/16	Wed 15/06/16	37																											
39				Wiki	85 days	Mon 29/02/16	Fri 24/06/16																												
40				Weekly report	85 days	Mon 29/02/16	Fri 24/06/16																												
41				State of the art	15 days	Mon 29/02/16	Fri 18/03/16																												
42				Final report	85 days	Mon 29/02/16	Fri 24/06/16																												

Project: ProjectPlanning Date: Tue 8/03/16	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

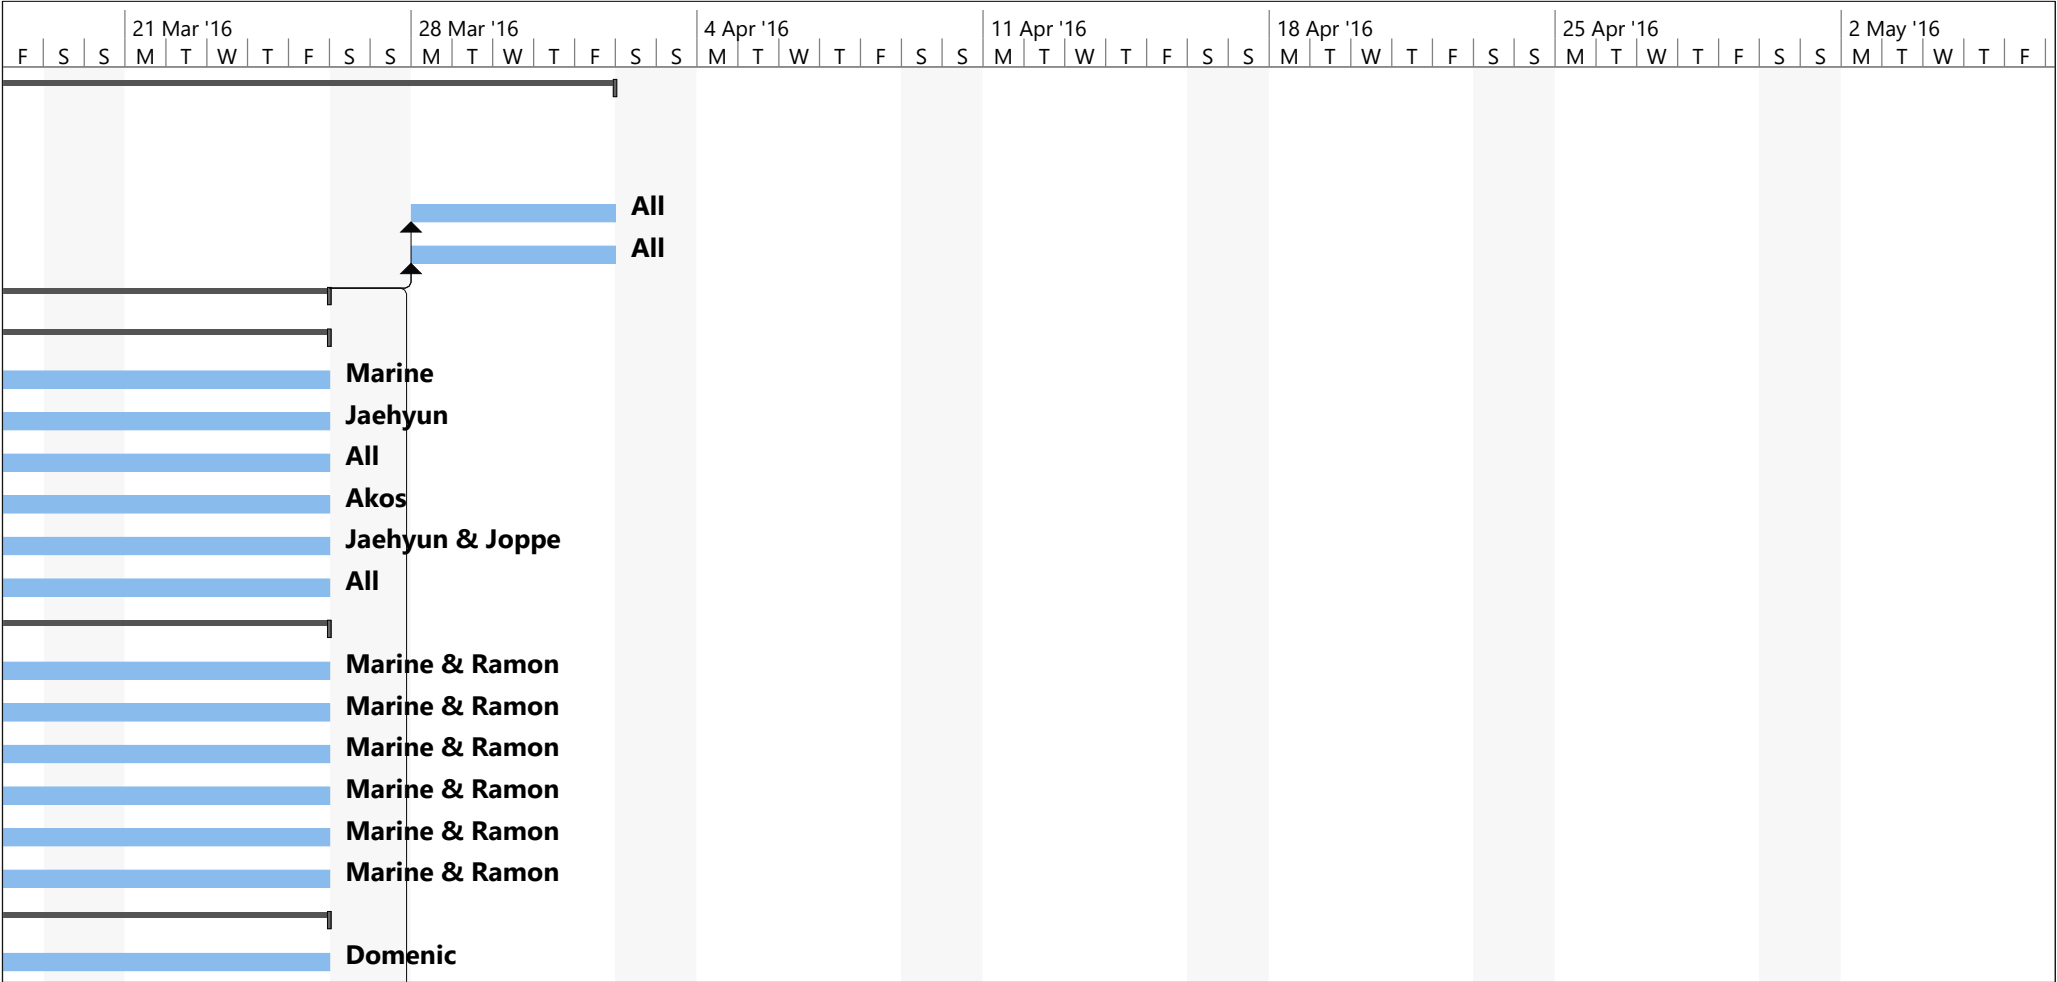


Project: ProjectPlanning
Date: Tue 8/03/16


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

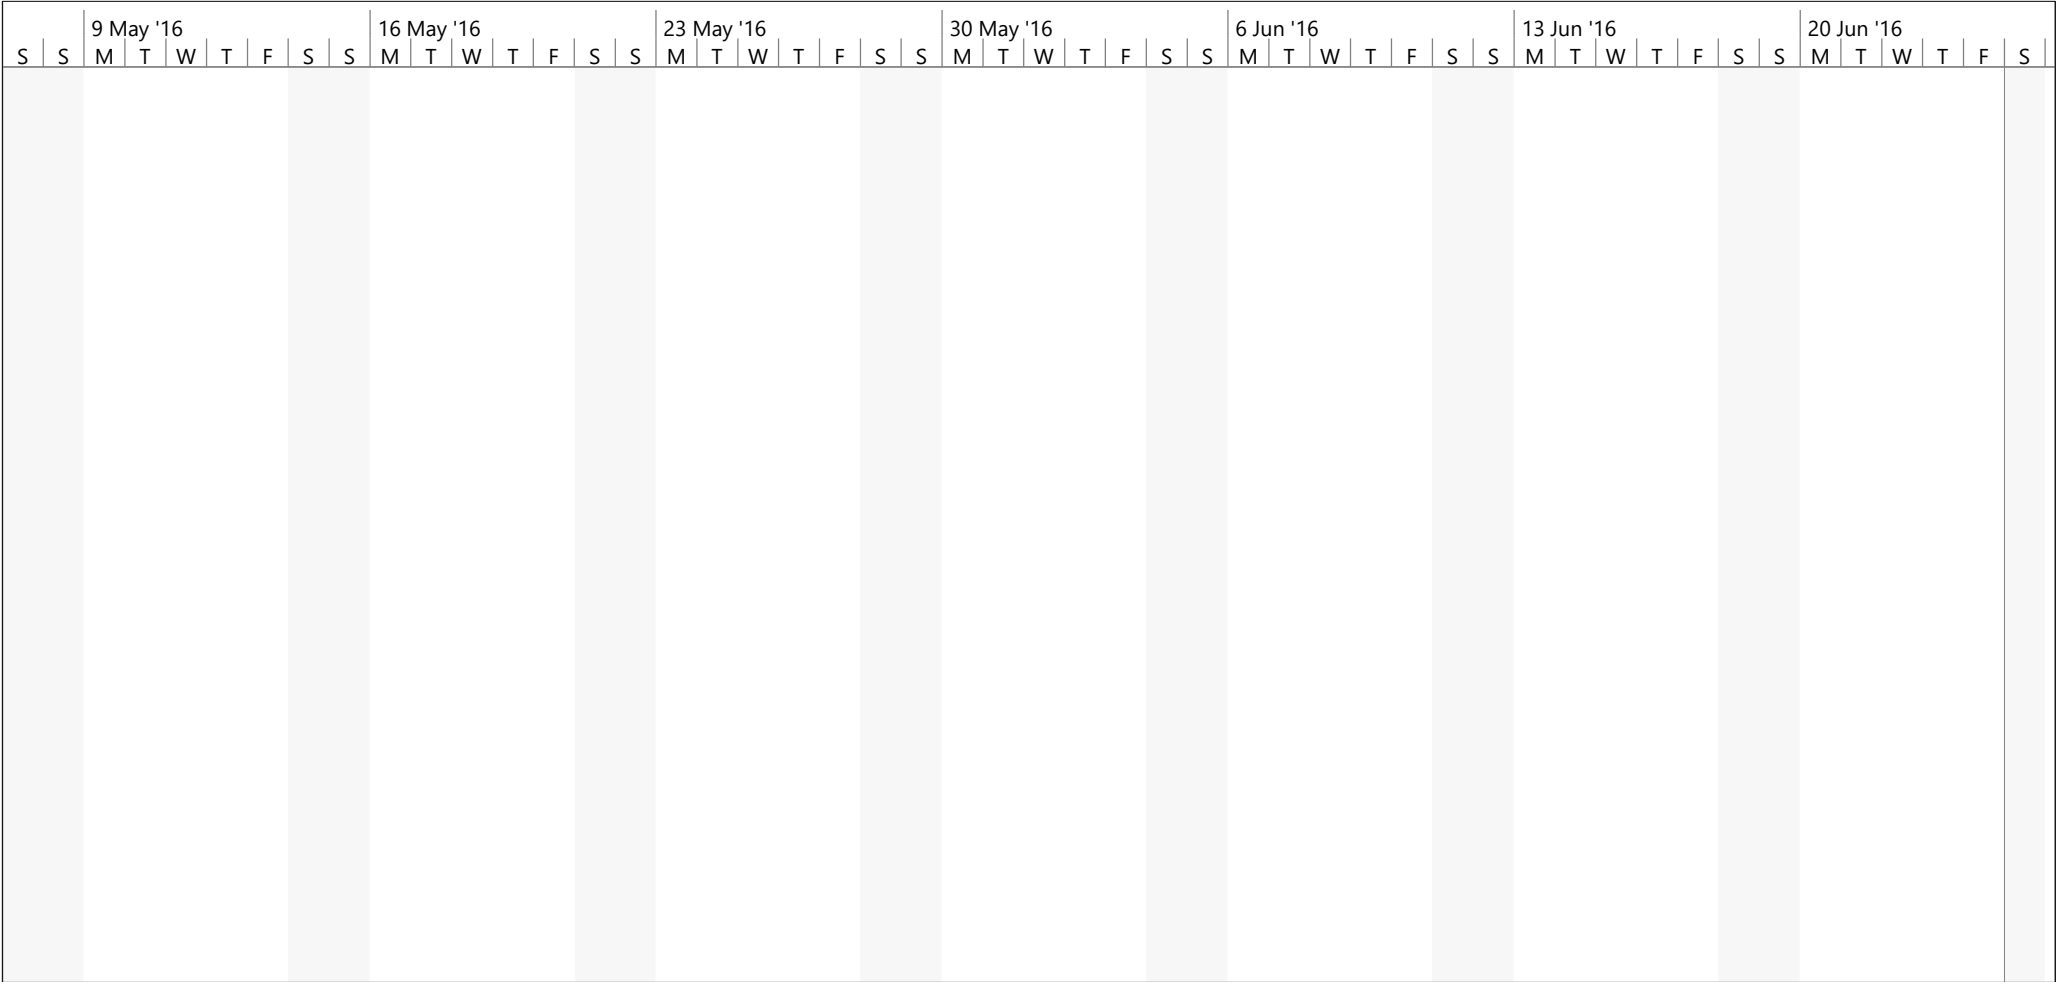

Project: ProjectPlanning
Date: Tue 8/03/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

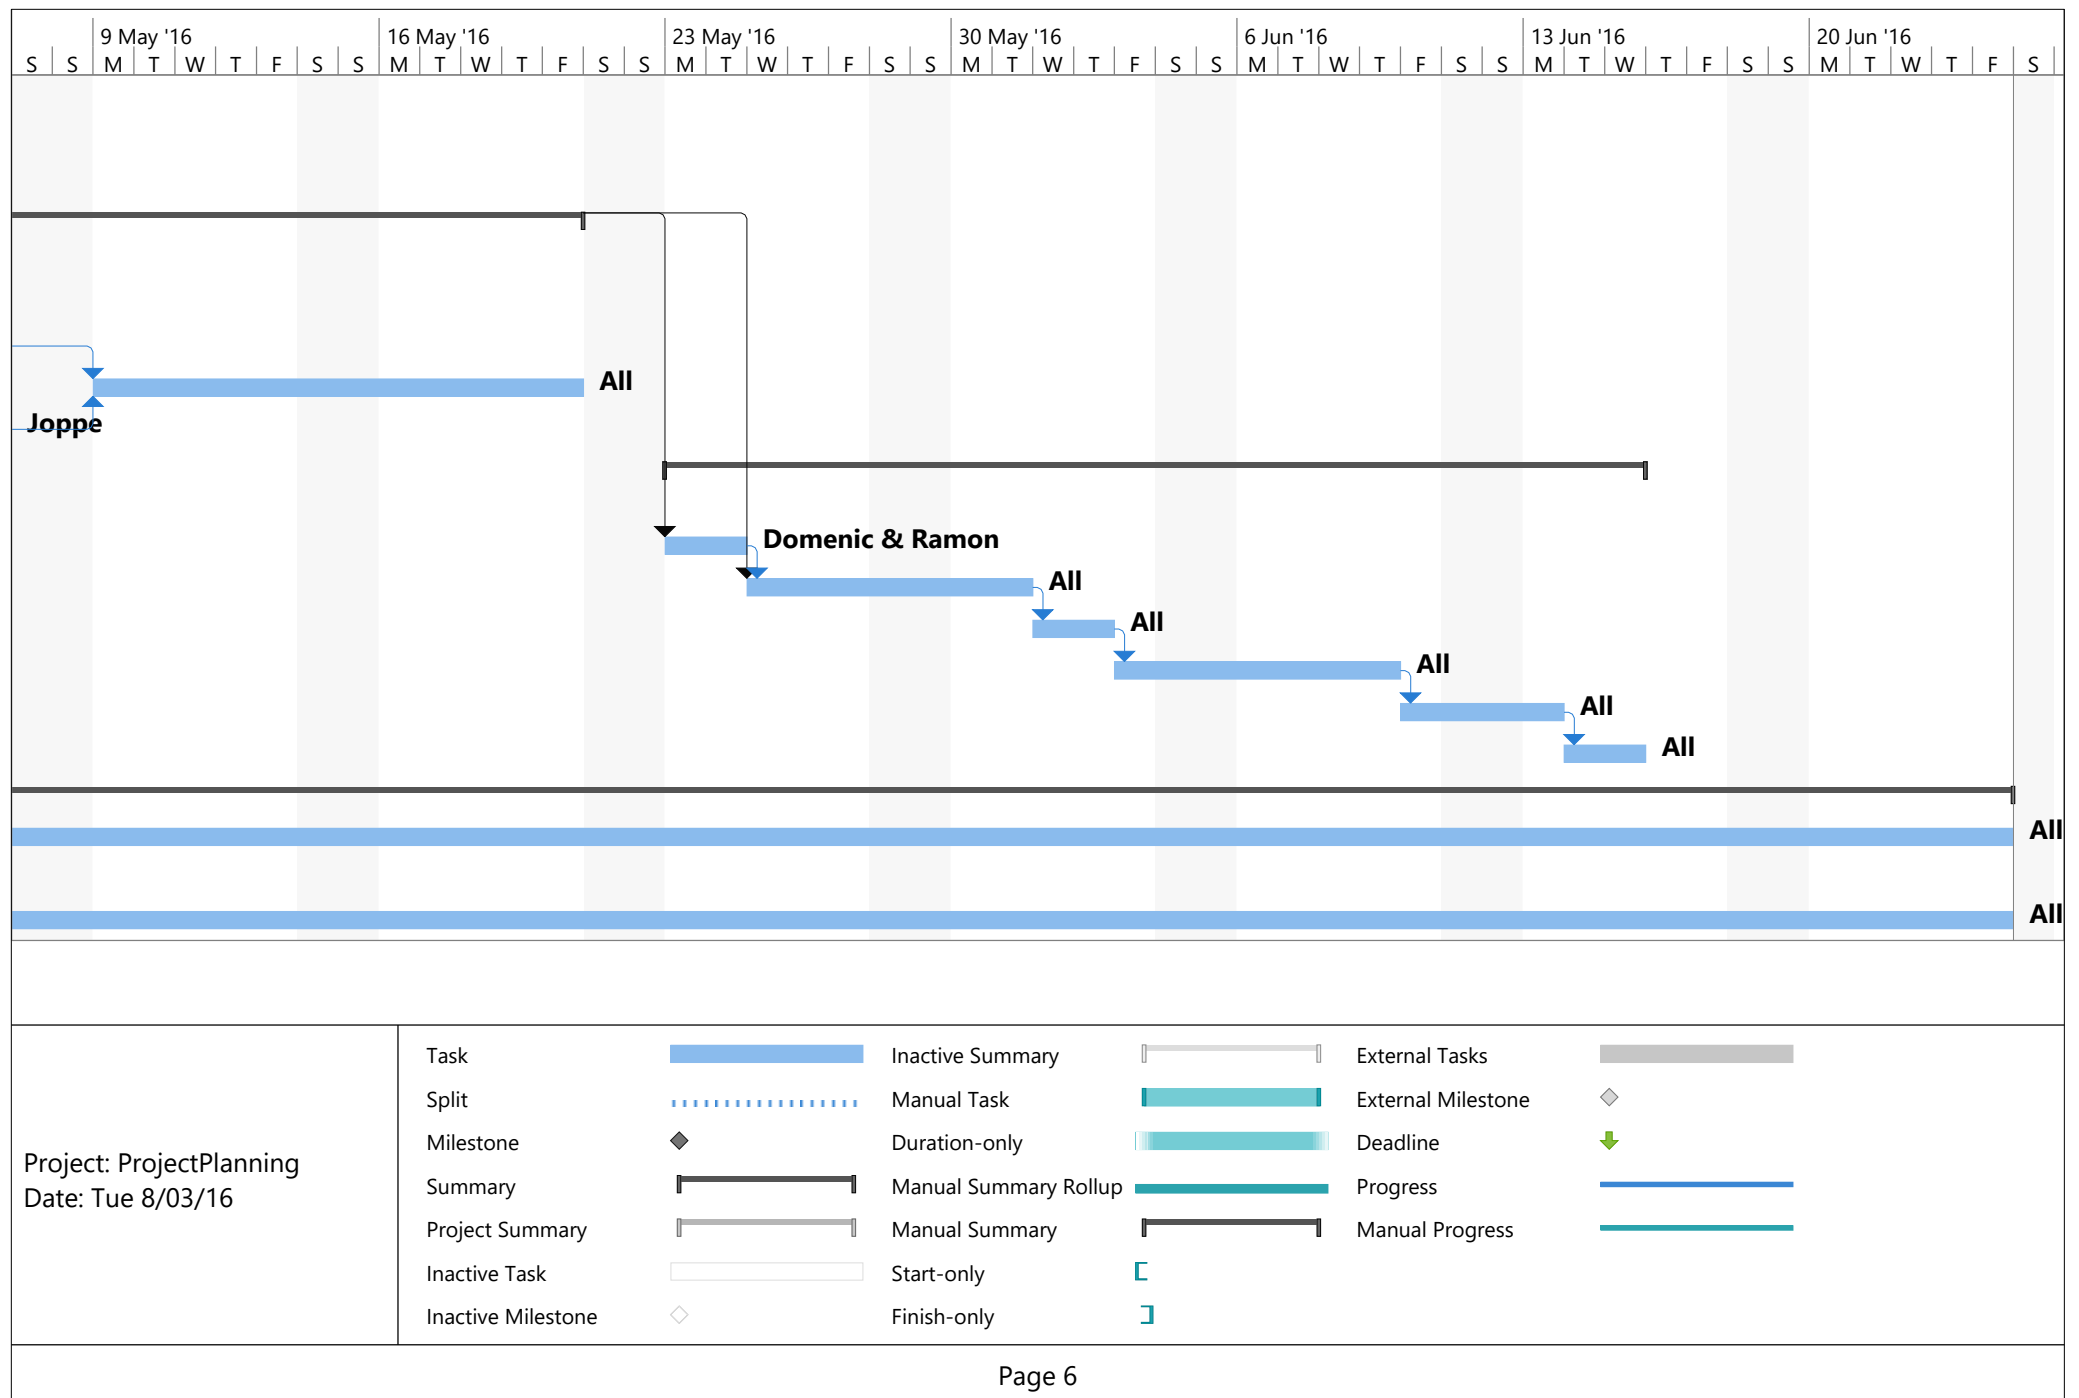

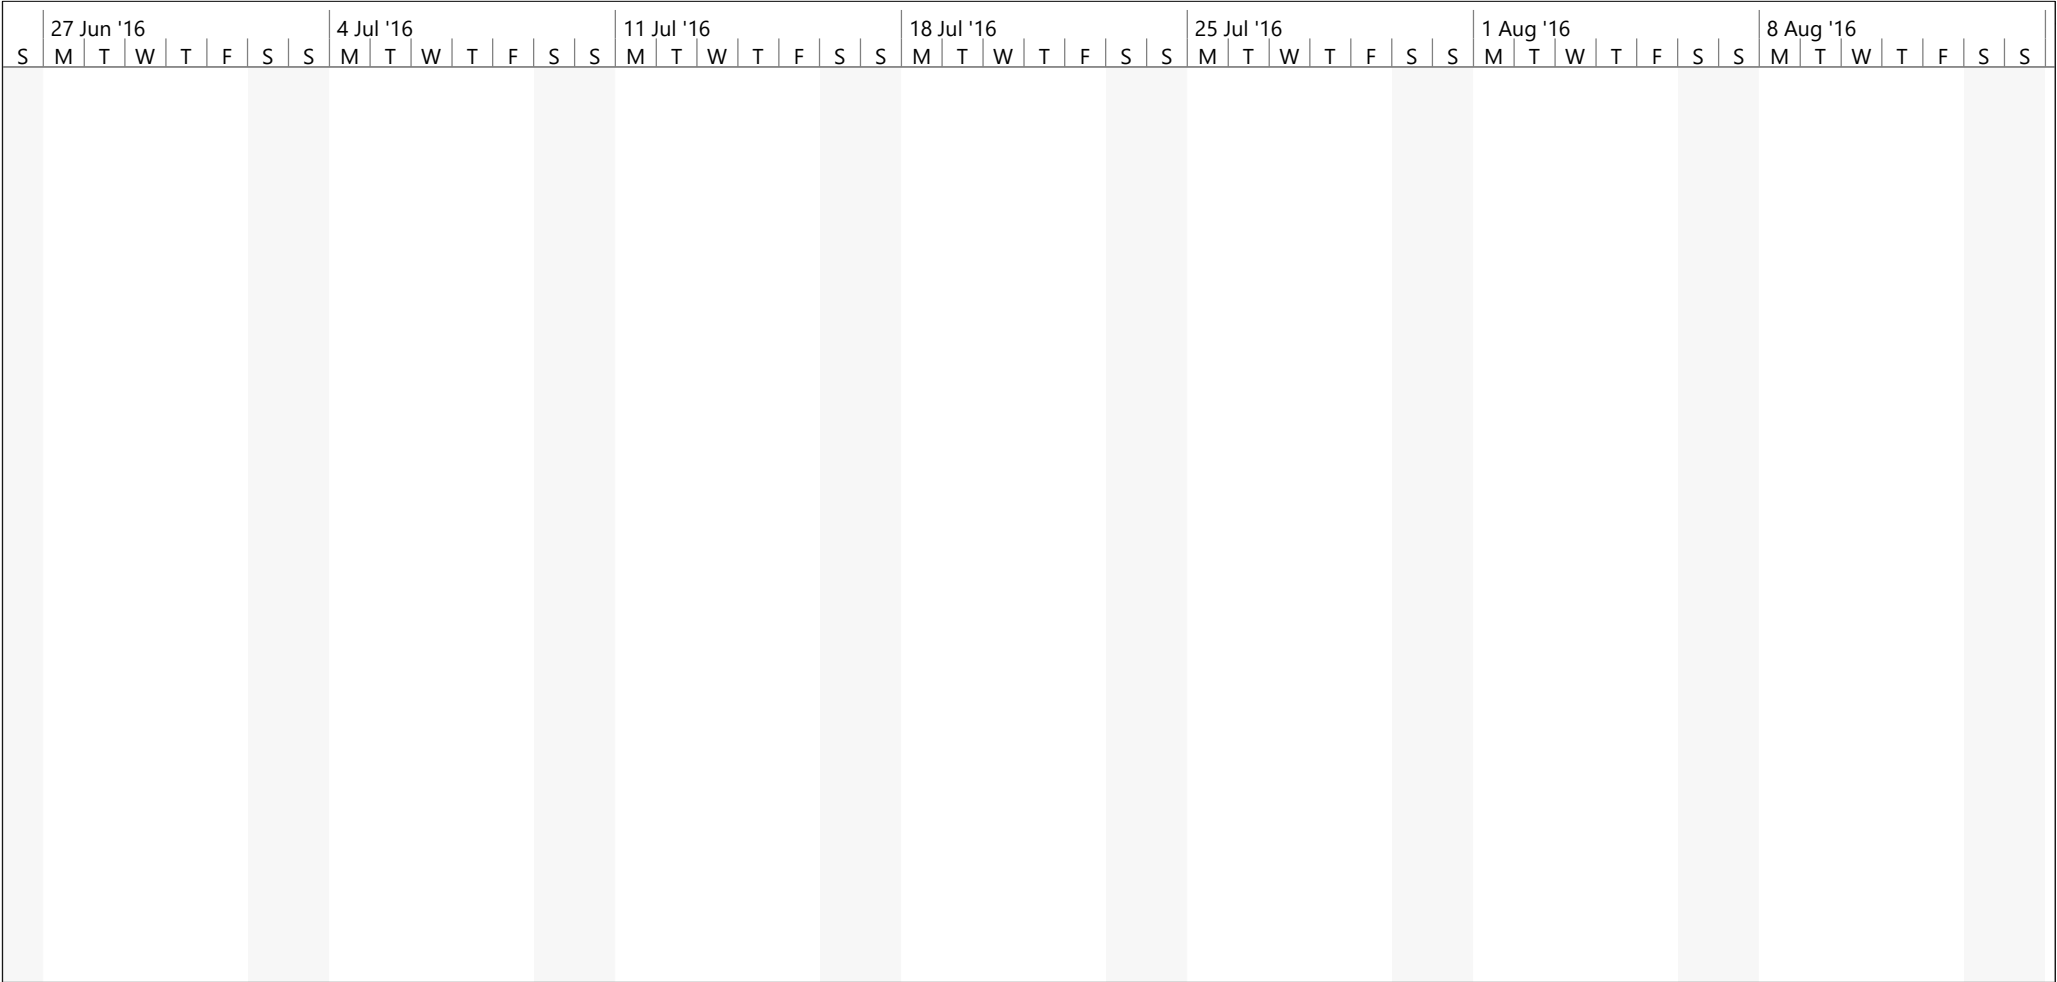

Project: ProjectPlanning
Date: Tue 8/03/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

